

SITE INSPECTION -- PHOTO DOCUMENTATION

Zava Telecom -- Field Operations

DOC-PHOTO-2026-05-02-TR9

Inspector: J. Alvarez | Date: 2026-05-02 | Site B, Segment 9



PHOTO 1: Vault TV-3 Interior
Conduit crack visible at 12 o'clock.
Water intrusion. Ref: FSE-2026-0041 SM-11.

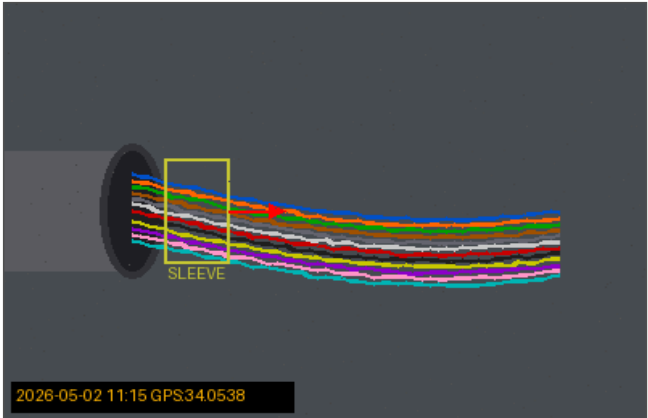


PHOTO 2: Cable Stress Point
Micro-bend at conduit entry.
Sleeve displaced 8cm. Micro-bend source.

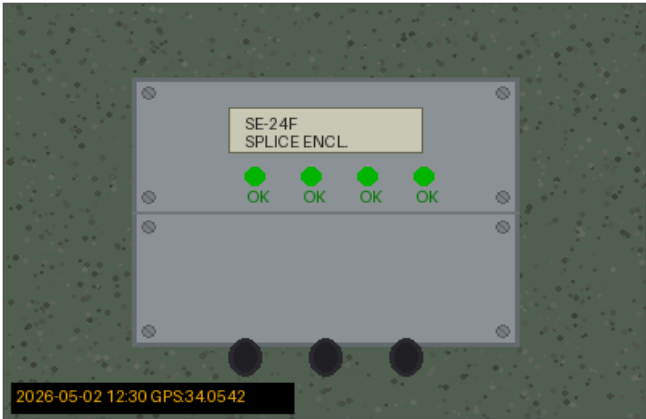


PHOTO 3: Splice Enclosure
SE-24F housing intact.
No moisture detected.

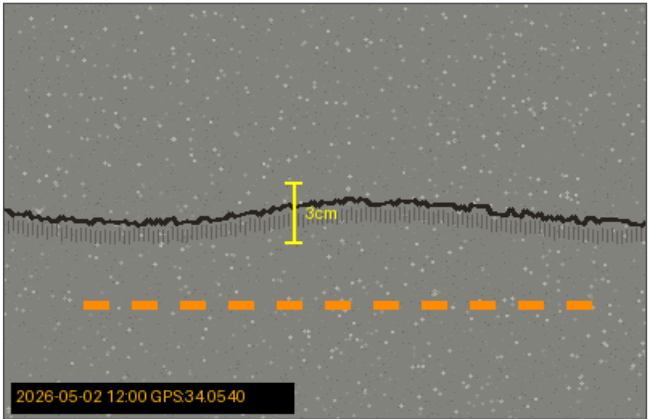


PHOTO 4: Surface Damage
Pavement heave above conduit.
3cm offset. Shared conduit (Rt1+Rt2).

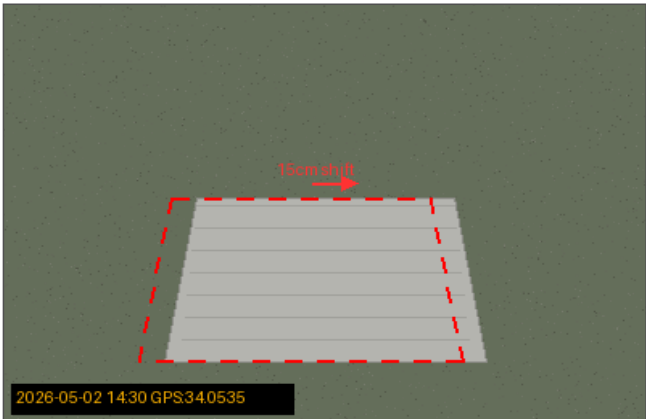


PHOTO 5: Barrier Status
Jersey barrier displaced
15cm from last survey.

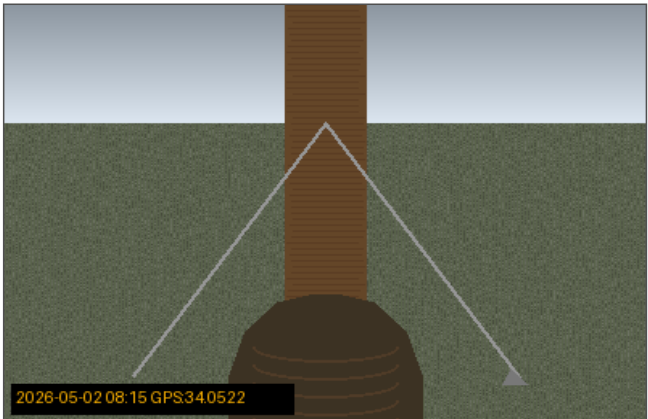


PHOTO 6: Pole TR-38 Base
Ground erosion at base.
Guy wire tension OK.

PRIORITY: Photos 1,2,4 critical -- 42 customers at risk (Rt1+Rt2 shared conduit Sec 3-5).

~~~~~

J. Alvarez, Lead Inspector  
Date: 2026-05-02

Refs: VID-IDX-2026-04-10-TR9 (VID-05), AUD-2026-04-15-TR9, FSE-2026-0041, FRD-2026-04-28
